



Approved By: _____

Contractor: Darr Construction
Project: Northport VA
Date: 07/03/2026
Manhole #: MH 7
Casting: Campbell 1012
Inspection: Suffolk County

**BASE SECTION
(RIGHT SIDE UP)**

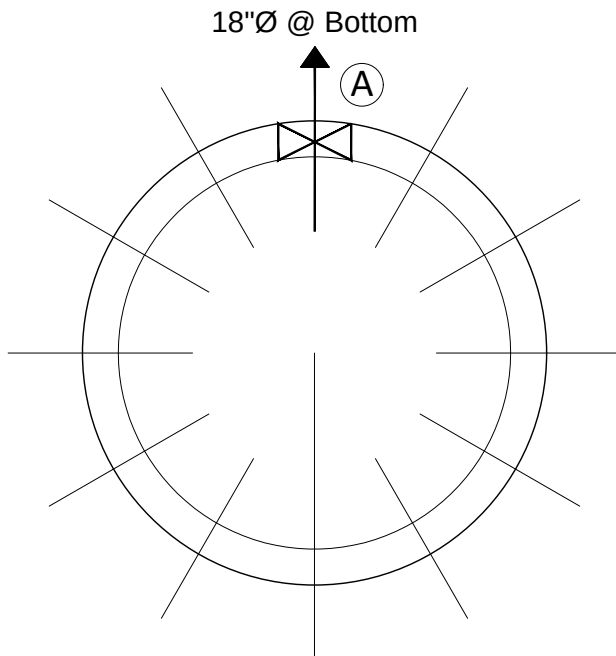

RISER

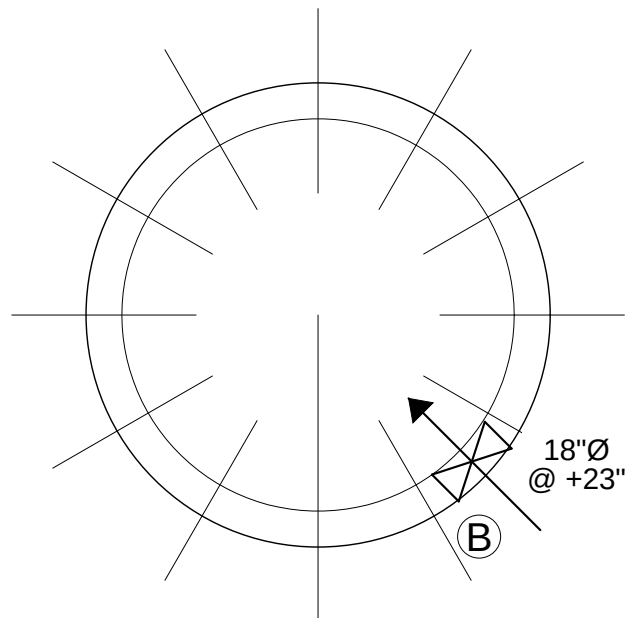

Rim Elevation Low 147.98
Invert 140.53
Invert to Top 7.45
Casting (-) 0.33
Top Slab (-) 0.67
Brick Adjustment (-) 0.20
Sump (+) 0.25
Wall Height 7.50

Use: 4 'Ø Use: 30"
Riser: 5'-0"

Brick Adjustment: 2 "

	INVERT	DIA	TYPE	BOOT
A	140.53	12"	HDPE HDPE	PSX-D18
B	144.98	12"	HDPE HDPE	PSX-D18
C				
D				

